

LOS ANGELES COUNTY CONGESTION REDUCTION DEMONSTRATION PROGRAM STATUS REPORT

Ad Hoc Congestion Pricing Committee

April 18, 2012



Metro

Transit Improvements: El Monte Station



Aerial Photograph: March 10, 2012

Transit Improvements: El Monte Station



Project Photographs: April 2012



Transit Improvements: El Monte Station



Scheduled to open August 8, 2012

Transit Improvements: Patsaouras Plaza Busway Station



- All technical studies complete
- IFB for Design/Build scheduled for Advertisement April 30, 2012
- Contract Award: August 2012
- Design Complete: May 2013
- Construction Starts: March 2013
- Project Complete: April 2014

Transit Improvements: Harbor Transitway

Completed CRD Projects

- Harbor Gateway Transit Center (HGTC) Sheriffs Substation
- HGTC CCTV System
- Station Lighting Improvements
- Slauson and Manchester Bus Stops

CRD Projects to Go

- Station CCTV and Transit Passenger Information System (August 2012)
- 37th Street Sound Barrier (August 2012)
- Non-CRD projects also include HGTC landscaping, automated public toilet, public art, and signage/wayfinding improvements (December 2012)



ExpressLanes Construction




ExpressLanes Construction



ExpressLanes Construction



ExpressLanes Construction

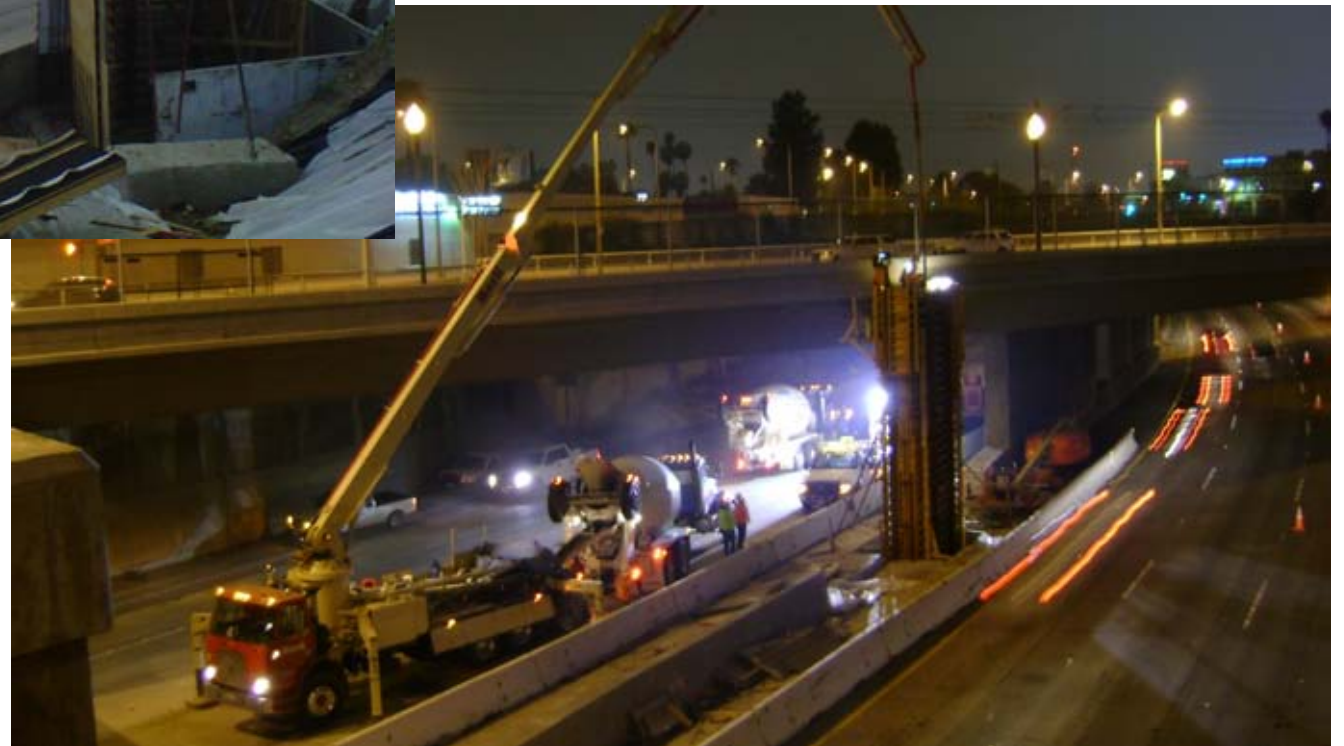

Program Milestones & Schedule

